



PROMETHEUS GROUP

◀Prometheus Platform: Web Planning & Scheduling Solution▶



GOLD FIELDS

Prometheus Group Enterprises, LLC,
1101 Haynes Street, Suite 218, Raleigh, NC 27604

CONFIDENTIAL

The contents of this document are confidential and are intended exclusively for Customers S. A. and its employees. Distribution or sharing of this information with persons or entities for which it is not intended is prohibited, in any form, without the express written consent of Prometheus Group.



Table of Contents

Table of Contents.....	2
Prometheus Company Overview	3
Proposed Solution.....	4
Customers Functional Requirements	12
Supplementary Aspects: Implementation, Project and Training Overview	17
Total Cost Breakdown	Error! Bookmark not defined.

Prometheus Company Overview

With 20 years of experience and 1,000+ implementations to date, Prometheus Group is a leading global provider of comprehensive and intuitive plant maintenance operations and optimization software, with a broad platform of solutions addressing the unique idiosyncrasies and requirements of heavy asset operators. Prometheus' interconnected platform allows changes to be communicated in real-time across an organization, improving manpower efficiency and driving production uptime.

Prometheus Group was founded in 1998 as an SAP consulting company. Since then the company has converted

from a consulting shop an enterprise application software company specializing in improving the usability and user adoption of SAP as well as other EAM software including Maximo and Oracle. Developed jointly with end users, our software enhances the customer experience with intuitive functionality, graphical visualization, and simple processes.

In 2017, Prometheus Group acquired PIPELINE Group and Sage Technology. The additions of PIPELINE proven Maxavera® and Syntempo® technology a Sage Technology extend the current solutions to include application integration, work execution for capital and outage, real-time schedule and electronic permitting for popular ERP and EAM enterprise applications (beyond SAP).

In 2018, Prometheus Group expanded its comprehensive suite of planning, scheduling, and mobility application for IBM's Maximo EAM system through the acquisitions of Solufy Information Technologies, Inc and DataSplice, LLC. Solufy is an Ottawa-based software company that has successfully developed a best of breed software solution for enhancing and simplifying planning, scheduling and data management in Maximo. DataSplice is an industry leading enterprise mobile platform solution provider, enabling companies to easily integrate their enterprise asset management systems with mobile devices, providing users the ability to access, view and update data from multiple sources on a single device.

In addition to a best-in-class software portfolio, Prometheus Group offers elite, high-end consulting and support services. These services include technical, functional, and business process training as well as implementation and master data consulting services. A dedicated Prometheus Support Team ensures continued success for our customers long after the initial implementation.

To meet the needs of an increasingly global customer base and marketplace, Prometheus Group maintains a global headquarters office in Raleigh, NC (USA) and regional offices in San Antonio, TX (USA), Fort Collins, CO (USA), Irvine, CA (USA), Leeds (UK), Berlin (Germany), Pretoria (South Africa), Sao Paulo (Brazil), Bogota (Colombia), Buenos Aries (Argentina), Brisbane (Australia), and Morwell (Australia). Our global executive leadership team and sales, customer support, and professional services leadership teams all reside in the Raleigh headquarters office.

SAP® Certified
Integration with SAP® S/4HANA



ORACLE® Gold Partner



Proposed Solution

Prometheus Platform | Web Planning & Scheduling Module


The Planning & Scheduling module of the Prometheus Platform provides web-based planning and scheduling products for routine maintenance management. It is an out-of-the-box solution that streamlines maintenance processes by using applications that fully integrate with your SAP PM system, keeping it the single source of truth for your data.

The Planning & Scheduling module was designed with user interaction in mind, implementing browser-based features that end users are familiar with and use every day. The solution enhances your out-of-the-box SAP PM. It includes a graphical maintenance scheduler, short cuts to saved searches in and out of the main SAP PM, a faster way to print work packages, and more. It maximizes your Planners' and Schedulers' efficiency on the job and can lead to a more proactive maintenance strategy.


The **Web Planning & Scheduling Solution** is a software suite consisting of the following solutions:

- *Scheduler*
 - Provides a graphical interface for Maintenance or Production orders
 - Simulate scenarios and auto-level Work Orders based on users' prioritization
 - Quickly reschedule work in a Calendar view
 - Manage and schedule to available resource capacities
- *Navigator*
 - Open SAP Transactions with Variants preloaded and skip the selection screen
 - Open Planning & Scheduling applications with pre-loaded search criteria
- *Work Package Manager*
 - Print or generate a PDF of selected documents associated with a work order
- *Order to Task List and BOM*
 - Generate a Task list from a Work Order
 - Update Bill of Materials with components assigned to the work order
- *Material Shopping Cart*
 - Search for materials with a "Google" like search across multiple SAP fields
- *Order Planner*
 - Simplified order view for basic updates to planned data
 - Access Order to Task List and BOM, Work Package Manager, and Material Shopping Cart while on the web


Navigator: Transform your SAP Favorites list to a custom layout with built-in variants that allow you to navigate your workflow progress more efficiently.



Prometheus Scheduler: Take control of your planned work with an easy-to-use graphical scheduler that includes simulation mode to run auto-level scenarios before saving to SAP, and mass change functionality to quickly update multiple work orders all at once

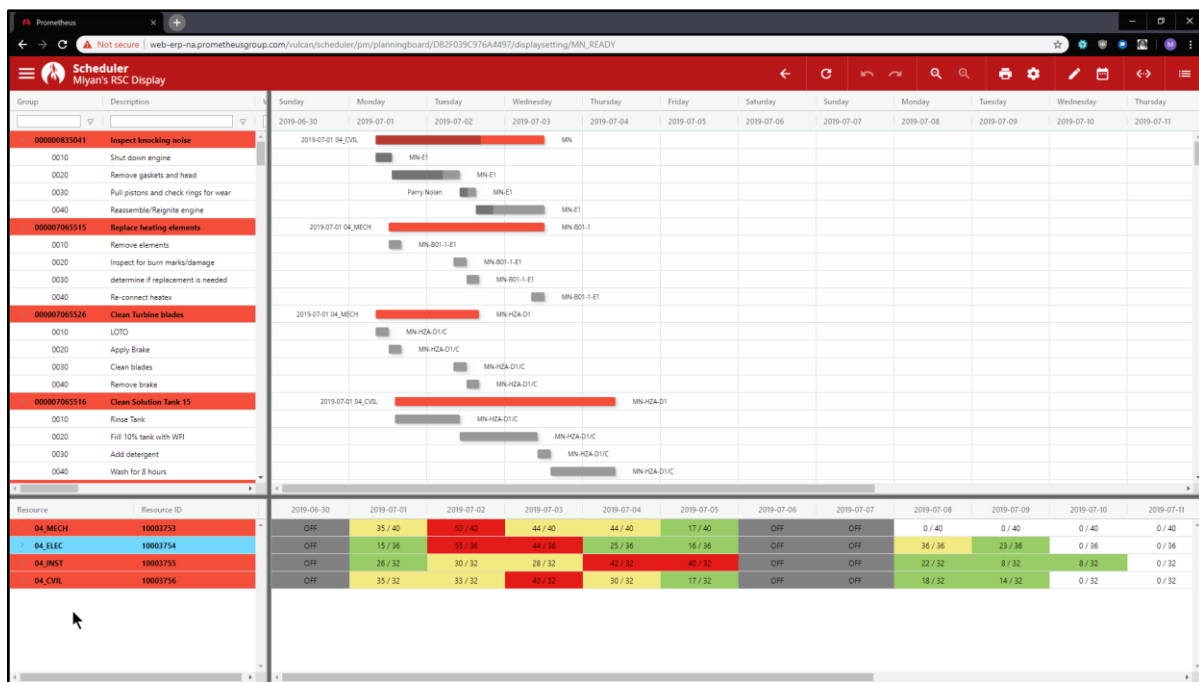

Prometheus Scheduler Auto-level capability: The functionality allows the user to select the orders to be auto leveled, indicate the date range, and to what capacity percentage to schedule the work centers to the selected operations. Prioritization is based on user-definition from the auto-level parameters screen.

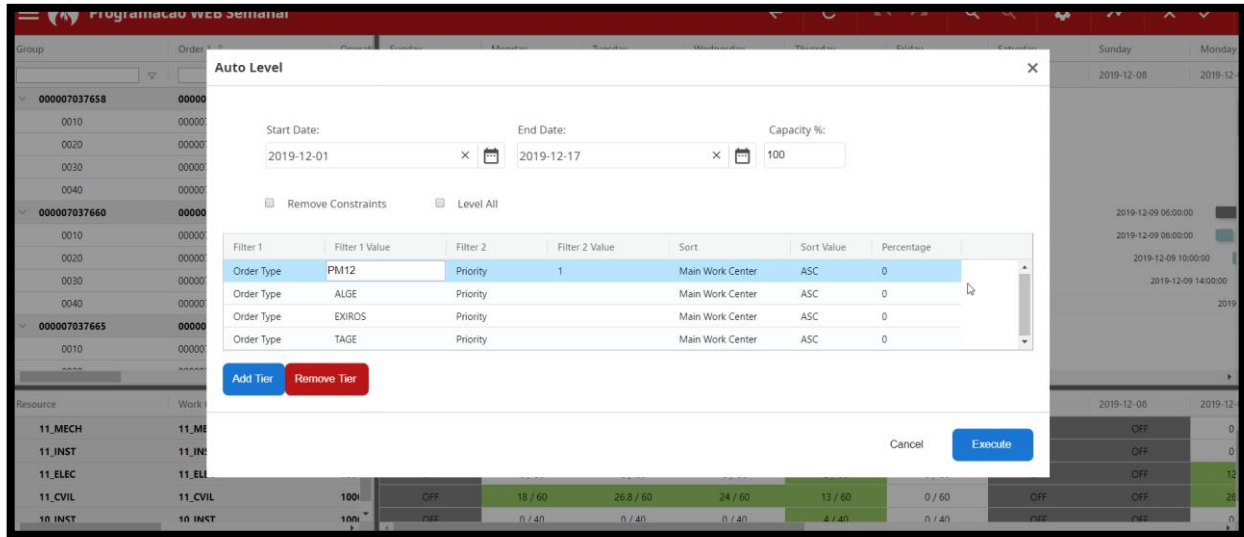

Auto Level

Start Date: 2019-12-01 End Date: 2019-12-17 Capacity %: 100


☐ Remove Constraints ☐ Level All

Filter 1	Filter 1 Value	Filter 2	Filter 2 Value	Sort	Sort Value	Percentage
Order Type	PM12	Priority	1	Main Work Center	ASC	0
Order Type	ALGE	Priority		Main Work Center	ASC	0
Order Type	EXIROS	Priority		Main Work Center	ASC	0
Order Type	TAGE	Priority		Main Work Center	ASC	0

Add Tier Remove Tier

Cancel Execute

Work Order Mass Change: Allows users to quickly modify work orders and operations via the List Edit Report. Users can modify any order level or operation level field, including user status and system status.

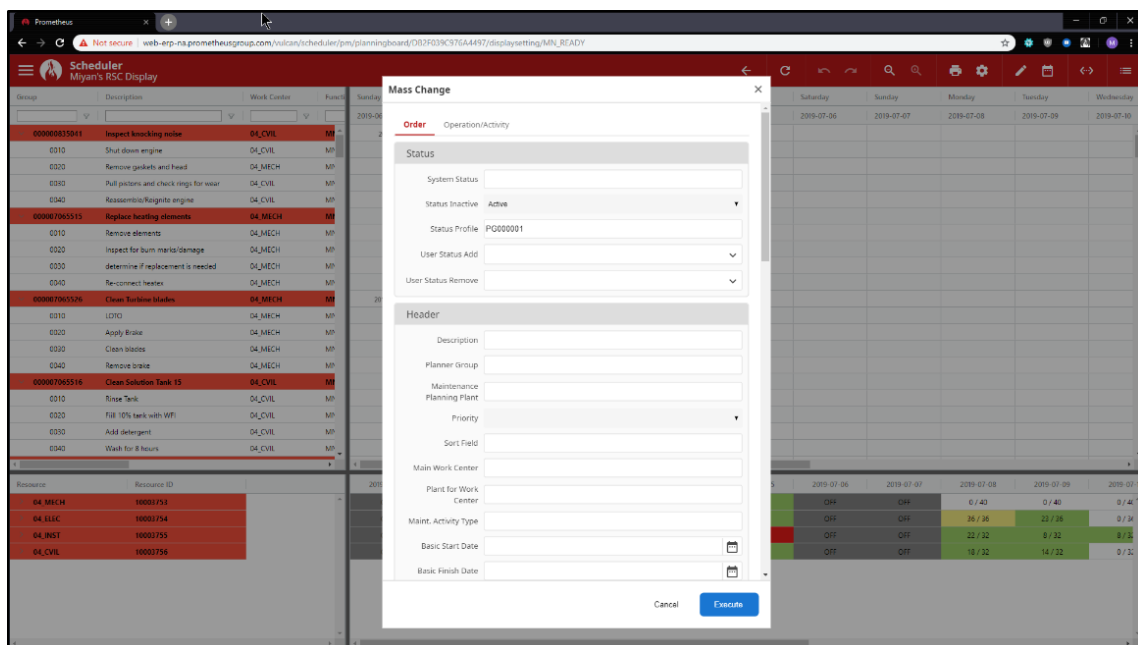

Mass Change

Order Operations/Activity

Status

System Status

Status Inactive Active

Status Profile PQ000001

User Status Add

User Status Remove

Header

Description

Planner Group

Maintenance Planning Plant

Priority

Sort Field

Main Work Center

Plant for Work Center


Maint. Activity Type

Basic Start Date

Basic Finish Date

Cancel Execute

Order to Task List: Takes an existing work order and converts it to a general, functional location, or equipment task list.

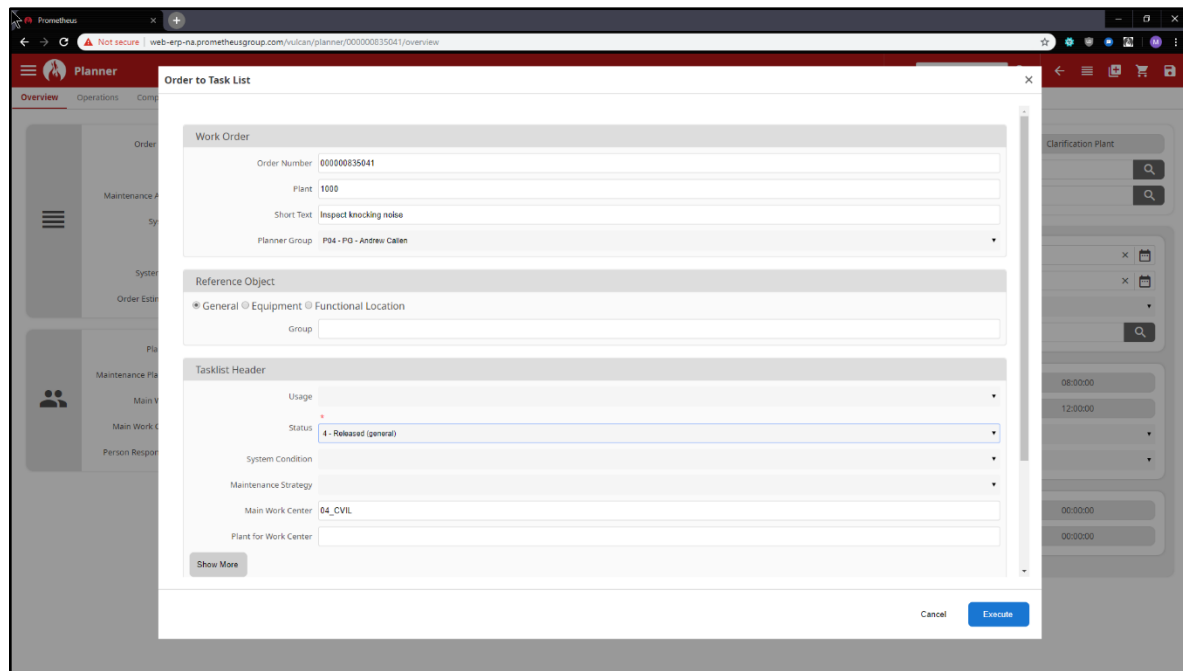


The 'Order to Task List' dialog box is displayed over the 'Planner' application interface. It contains the following fields and sections:

- Work Order:**
 - Order Number: 00000035041
 - Plant: 1000
 - Short Text: Inspect knocking noise
 - Planner Group: PG4 - PG - Andrew Caten
- Reference Object:**
 - General ☒ Equipment ☐ Functional Location
 - Group: (empty)
- Tasklist Header:**
 - Usage: (empty)
 - Status: 4 - Released (general)
 - System Condition: (empty)
 - Maintenance Strategy: (empty)
 - Main Work Center: 04_CVIL
 - Plant for Work Center: (empty)

Buttons at the bottom: Show More, Cancel, Execute.

Order to BOM: Allows the user to create a Bill of Materials from an existing work order. Order to BOM drives efficient maintenance planning.

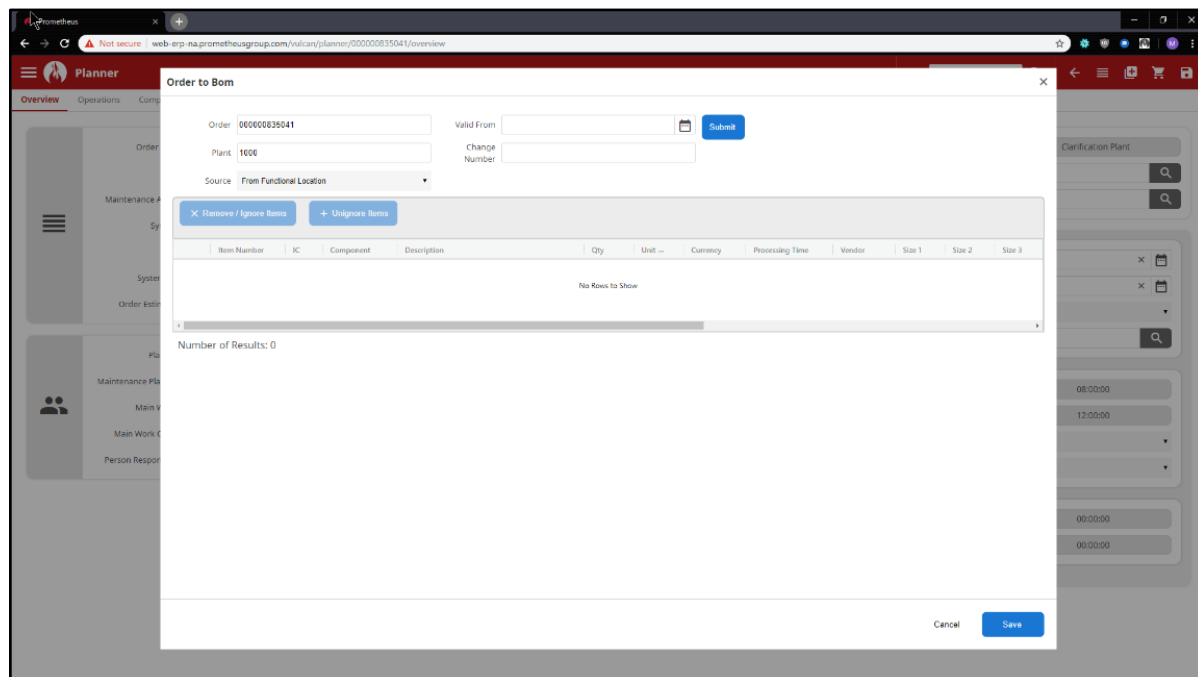


The 'Order to Bom' dialog box is displayed over the 'Planner' application interface. It contains the following fields and sections:

- Order: 00000035041
- Valid From: (empty)
- Plant: 1000
- Change Number: (empty)
- Source: From Functional Location
- Buttons: Remove / Ignore Items, Add Ignore Items
- Table:


Item Number	IC	Component	Description	Qty	Unit	Currency	Processing Time	Vendor	Size 1	Size 2	Size 3
No Rows to Show											
- Number of Results: 0

Buttons at the bottom: Cancel, Save.

Material Shopping Cart: A Google-like search that allows users to quickly perform multiple searches using single word, multi-word or any-order search within SAP and retrieve multiple materials from a single screen and transferred directly to the work order with a single click. Due to the ability to search on long text descriptions with MSC, free text material requisitions and free text spending is minimized.

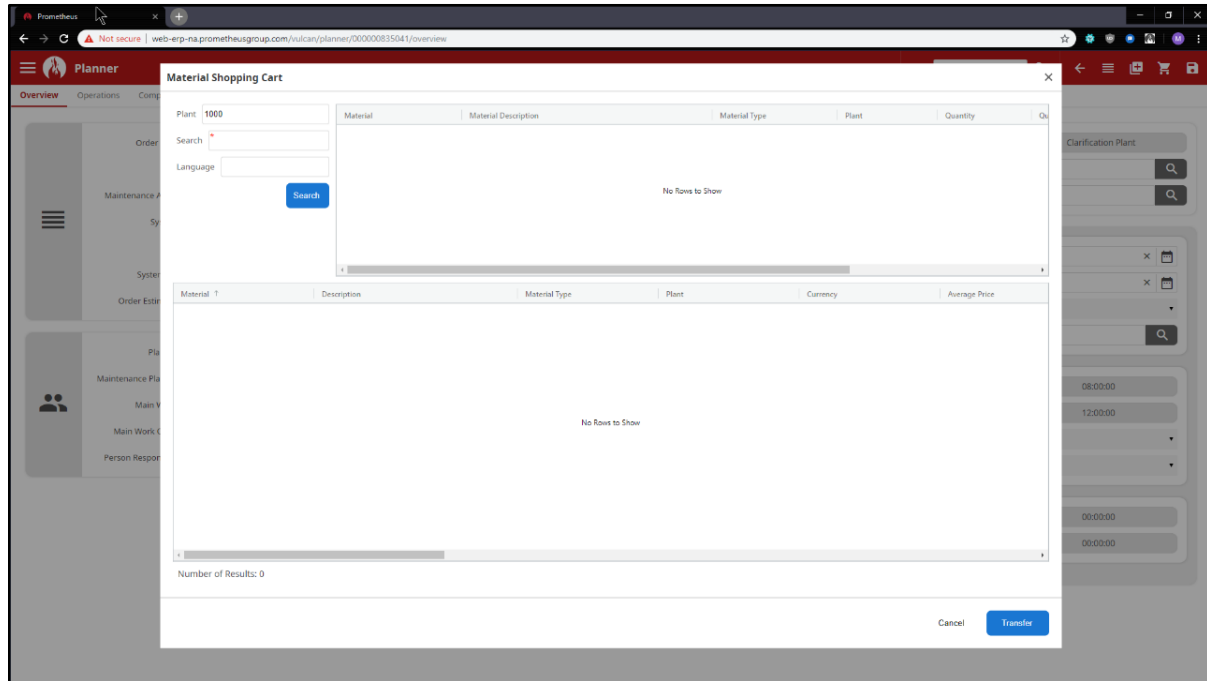


Work Package Manager: Work Package Manager gathers documents on the work order itself (shop papers, functional location, equipment, materials, and operations' document PRT's) and gives you the ability to print these individually or multiple work orders with one click.

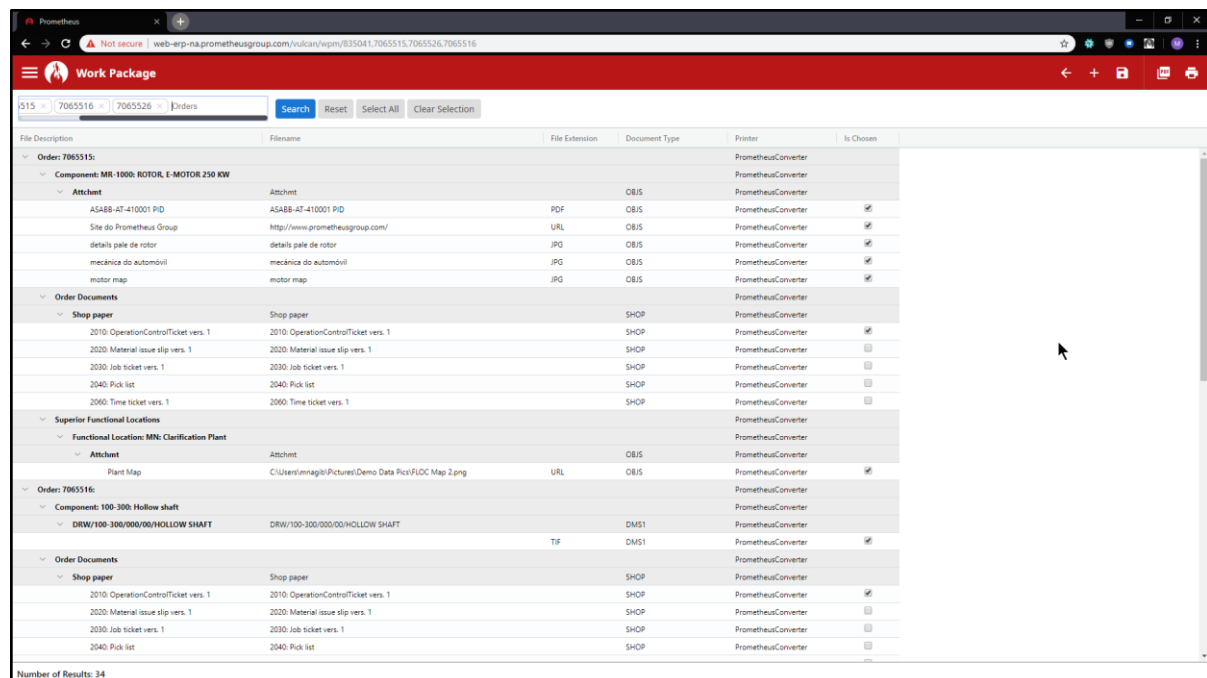

Additional Developments in Web Scheduler Specific to Customers

1. **Custom field in Scheduler Layout and the Scheduler Auto-Level Prioritization** – Customers has a custom field in their equipment master data that is imperative to their work prioritization. This field should be present within the Scheduler layout as well as available in the Auto-level feature, as seen in the example below. *Estimated Development Time: 15 days*

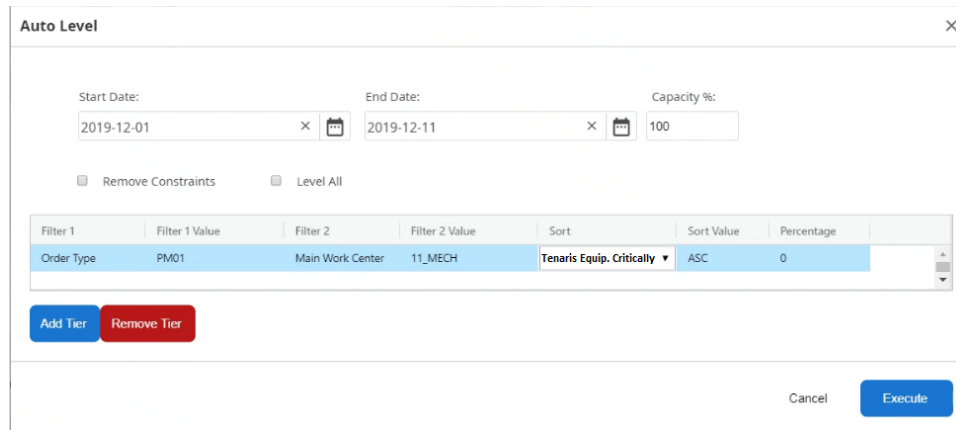

Auto Level [X]

Start Date: 2019-12-01 [X] [Calendar Icon] End Date: 2019-12-11 [X] [Calendar Icon] Capacity %: 100


☐ Remove Constraints ☐ Level All

Filter 1	Filter 1 Value	Filter 2	Filter 2 Value	Sort	Sort Value	Percentage
Order Type	PM01	Main Work Center	11_MECH	Tenaris Equip. Critically ▼	ASC	0

Add Tier **Remove Tier**

Cancel **Execute**

2. **Saving Variants within the Auto-Level Feature** – Users must be able to save and select auto-level prioritization criteria to use in future cases. The ability to save and select variants from within the auto-level feature will be added to the auto-level pop-up screen. Please see the proposed model below. *Estimated Development Time: 20 days*

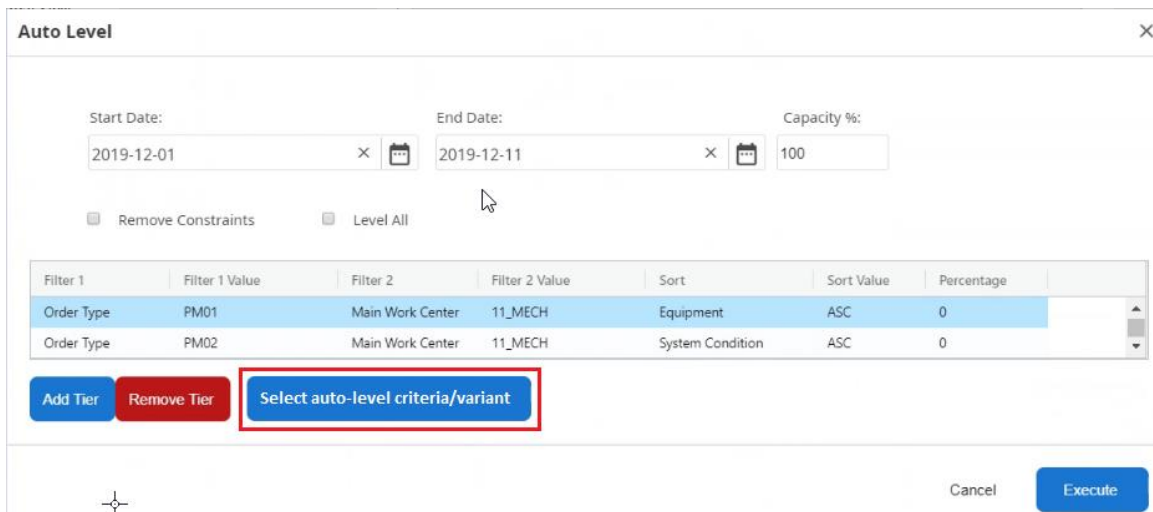

Auto Level [X]

Start Date: 2019-12-01 [X] [Calendar Icon] End Date: 2019-12-11 [X] [Calendar Icon] Capacity %: 100

☐ Remove Constraints ☐ Level All

Filter 1	Filter 1 Value	Filter 2	Filter 2 Value	Sort	Sort Value	Percentage
Order Type	PM01	Main Work Center	11_MECH	Equipment	ASC	0
Order Type	PM02	Main Work Center	11_MECH	System Condition	ASC	0

Add Tier **Remove Tier** **Select auto-level criteria/variant**

Cancel **Execute**

3. **Weighing Column in List Edit** – Users must be able to weight their orders according to some criteria and assign a value according to a Formula:
- Priority
 - Location
 - % Complete
 - Activity Type
 - Functional Location

Once all valued have been assigned, they would like to see the column in the List Edit and use the Auto-leveling functionality based on this Weighing Column Values (“Ponderación”).

Estimated Development Time: 20 days

Trabajos Semanales Trabajos Semanales Layout								
Arrastre aquí para establecer grupos de filas								
Orden 1 ↑	Descripción	Clase de orden	Ponderación	Porcentaje Completo	Estado sistema	Prioridad	Puesto de trabajo	Equipo
7067548	Inspección Inicial	PG03	9,000	25	PCNF REL	1	58_MC1	000000000010013293
7067548	Chequeo de parte 1A	PG03	9,000	50	PCNF REL	1	58_MC1	000000000010013293
7067548	Reparación y balanceo	PG03	9,000	17	PCNF REL	1	58_MC1	000000000010013293
7067548	Instalación de parte	PG03	8,750	20	PCNF REL	1	58_MC1	000000000010013293
7067548	Pruebas finales	PG03	8,500	50	PCNF REL	1	58_MC1	000000000010013293
7067549	Desmontaje de la bomba	PG03	8,000	100	PCNF REL	1	58_MECH	000000000010013293
7067549	Desarme de la bomba	PG03	8,000	100	PCNF REL	1	58_MECH	000000000010013293
7067549	Lubricación sellos	PG03	8,000	33	PCNF REL	1	58_MECH	000000000010013293
7067549	Lubricación empaquetados	PG03	7,500	25	PCNF REL	1	58_MECH	000000000010013293
7067549	Armado de Bomba	PG03	7,250	50	PCNF REL	1	58_MECH	000000000010013293
7067549	Montaje de Bomba	PG03	7,000	50	PCNF REL	1	58_MECH	000000000010013293
7067550	Desmonstar aspa de rotor	PG03	6,2750	20	PCNF REL	2	58_ELEC	000000000010013293
7067550	Desarmar aspa	PG03	6,200	17	PCNF REL	2	58_ELEC	000000000010013293
7067550	Limpieza aspa	PG03	6,200	67	PCNF REL	2	58_ELEC	000000000010013293
7067550	Armado de aspa	PG03	6,000	33	PCNF REL	2	58_ELEC	000000000010013293
7067550	Montaje de aspa en rotor	PG03	6,000	50	PCNF REL	2	58_ELEC	000000000010013293

Business Benefits associated with the web-based Planning & Scheduling Module:

VISUAL LAYOUT

- Scheduler’s graphical design and the ability to lay out maintenance work visually helps users see the work and plan it.
- This visibility allows Schedulers to make better scheduling decisions that improve efficiency, resource utilization, and ultimately, wrench time.
- Techs and Supervisors have a published schedule with any dependencies graphically shown, without having to go into a ERP/EAM/CMMS.
- Other visual elements are the heat maps. Visibility into the available labor hours and schedule capacity allow for better resource utilization and management.
- Able to schedule enough work for the week without over or under scheduling.
- Auto Level the schedule based on capacity parameters to give users a quick first pass at building out their schedules.

STANDARDIZE WORK PLANNING

- Can eliminate individual workflows and processes that are not consistent across the business.
- Build role-based navigations that follow a specific workflow to align your users.

STREAMLINE PLANNING AND SCHEDULING TASKS

- Other CMMS can be “clunky”, making it time-consuming, repetitive, and frustrating to complete simple tasks.
- Web WPM offers a quick and easy way to print and manage work packages.
- Order to Task List and BOM allows for easy updating of Bill of Materials (BOM) without having to enter the CMMS and for easy creation of Task list without having to enter the CMMS.
- Simplified search screens allow for less cumbersome or daunting selections screens and quick text searches on any field make it easy to pinpoint data.
- Make updates to shifts right from Scheduler with an intuitive right-click.
- Quick and easy drag and drop for grouping and sorting.
- Auto-Scroll and Auto-Refresh for communicating/viewing the schedule.

INCREASE USER ADOPTION

- Updated graphics allow for a more modern look and feel.
- More intuitive UI/UX than a CMMS.
- Standard navigation/UI/UX aligns with other Prometheus Web products and other applications used daily.
- Simplified user interactions make it easier and faster to use, as well as to learn/train/rollout.
- Ease of access: Can have individual browser links for specific schedules or any other aspects of the solution.
- Display Settings give more power to the user to make Scheduler fit their needs: more color options, multiple labels on bars, hover over information, etc.
- More configurable to meet custom requirements.

INTEGRATES WITH PROMETHEUS PLATFORM

- Prometheus Platform | Planning & Scheduling can scale with your business and integrate with the other modules of the platform.

PERFORMANCE & FUNCTIONAL ADVANTAGES

- Performance improvements: Accessing data directly gives us opportunities to improve on performance.
- Flexible to grow and account for fluctuating bandwidth demands.
- World-class disaster recovery.
- Easier to perform updates.
- No major capital-expenditures (servers, UPS, cooling)
- Prometheus can host the solution for an additional annual fee

Customers Functional Requirements

Customers has defined aspects and details on functional characteristics desired within a scheduling software solution. The following table contains these scenarios and the ways in which the Prometheus Scheduling solution suffices these functions.

Aspect	Detail	Prometheus Group Response
<u>1. Functional Scenario</u>	1.1. Scheduling of resources as work centers, work areas and people.	<i>Prometheus Planning & Scheduling</i> is a flexible interface to allow accurate resource capacity scheduling at the work center, area and individual personnel level. This is adjustable for different users or roles.
	1.2. Select scheduling range and frequency: allow the user to decide, for example, schedule weekly, with a range of a month.	<i>Prometheus Planning & Scheduling</i> users can determine whatever range they'd like to schedule to. This can be configurable to the Navigator to display different weekly, monthly or other schedule queues.
	1.3. Schedule Emergencies over scheduled work orders: allow the user to modify the work order's schedule in order to prioritize emergencies.	Work Prioritization can be facilitated in several manners within the <i>Prometheus Planning & Scheduling</i> solution, such as Sorting capabilities, drag and drop functionality, and auto-scheduling (Auto-Level) based on priority entries.
	1.4. Decide which Backlog work orders can be added to the schedule.	Variants to exploit and identify incomplete Work Orders can be established to quickly access your Backlog. From there scheduling, direct edit, and mass change capabilities facilitate adding backlog Orders to the current schedule.
<u>2. Usability</u>	2.1. Data selection / variant selection: manufacturing center, work order, responsible work center, planner group and revision.	Any field, including custom fields can be leveraged from the Prometheus Scheduler Selection Screen and saved as Variants.
	2.2. Drill into work orders to view and change details: allow the user to drill up and down to review different levels of data.	The Prometheus Order Planner enables full visibility into individual Work Order details in a simple user interface. The Scheduling solution also supports direct access to SAP from the Prometheus environment.
	2.3. Mass change system and user status: allow the user to massively	Prometheus Mass Change allows modification of over 140 fields at the

change status and user status.	Operation and Order level, including User and System Status
2.4. Mass change work order header data: allow the user to massively change header data.	Prometheus Mass Change allows modification of over 140 fields at the Operation and Order level.
2.5. Mass change operation user's status: allow the user to massively change operation user's status.	Prometheus Mass Change allows modification of over 140 fields at the Operation and Order level, including User and System Status
2.6. Mass change operation data: allow the user to massively change operation data.	Prometheus Mass Change allows modification of over 140 fields at the Operation and Order level.
2.7. Mass change scheduling dates and time: allow the user to massively change dates and time.	Prometheus Mass Change Dates & Times allows scheduling of multiple Work Orders simultaneously.
2.8. Material status check: allow the user to check material status in real time.	The <i>Prometheus Planning & Scheduling</i> solution features a <i>Material Availability Coordinator</i> add-on to facilitate material coordination and planning around the maintenance scheduling process. This solution enables real time material check and integrates directly with the Scheduler.
2.9. Drag and drop for scheduling and assigning work centers: allow the user to drag and drop work orders into work centers, days, etc.	Drag and drop Scheduling, Work Center and personnel assignments are supported with the Prometheus Scheduler.
2.10. User friendly visualization: visual interface easy to read, understand and use by the user.	The Prometheus Scheduler visually and intuitively represents the Work Order details from your SAP system to provide a facilitated means of scheduling and capacity resource planning.
2.11. User customization capability: allow the user to customize the system according to his/her needs and preferences.	The <i>Prometheus Planning & Scheduling</i> is highly configurable to the users' needs at a functional level and user-interface/visual level. This includes configurability in regard to the Navigator, the Scheduler, List Edit, etc.
2.12. Multiuser log-in and process: allow several users to access the system at the same time.	Any and all users with access to the solution have access at any point in time.
2.13. Ease of use with SAP: ease of use	Prometheus solutions are directly

	between the scheduler and other SAP screens.	integrated with SAP. The Scheduler makes changes with SAP data in real time and allows drill into the associated transaction codes. The Navigator allows users to access any SAP screen to create 1-click access to relevant list views.
<u>3. Planning</u>	3.1. Manual planning of work orders: allow the user to manually plan work orders.	The Prometheus Order Planner enables full visibility into individual Work Order details in a simple user interface with the ability to plan and modify any desired field.
	3.2. Manual planning of operations: allow the user to manually plan operations.	The Prometheus Order Planner enables full visibility into individual Work Order details in a simple user interface with the ability to plan and modify any desired field including adding and modifying operations.
	3.3. Automatic planning simulation: allow the user to automatically simulate the delivery date of work orders according to resource availability and taking into account all the work orders together. The user shall be able to freely customize the prioritization policy of work orders by combining some of the criteria listed above.	Simulation mode and Auto-Level capabilities allow simple creation of a resource-loaded schedule with respect to Work Center capacity and resource availability. Strategic methods can be incorporated, so Work Orders are scheduled by priority, preventive vs corrective, etc.
<u>3. Planning</u>	3.4. Apply relationships between operations: allow the user to define different types of relationships (start-end, end-start, start-start, end-end), insert milestones and view critical path.	Operation Relationships can easily be added, modified, or removed from the Prometheus Scheduling solution to ensure jobs are sequenced accurately and appropriately. Critical path identification is on the development roadmap to be completed by the end of the 2019 calendar year.
<u>4. Scheduling</u>	4.1. Schedule orders and operations in Gantt format.	This is the standard format of the Prometheus Scheduler
	4.2. Identification of different work types: allow the user to differentiate between planned, emergency and backlog work orders.	The same fields used to distinguish Work Order types can be viewed and leveraged from the Prometheus environment for better insight into strategic scheduling.
	4.3. Automatic scheduling of operations / work orders: schedule operations and work orders	Prioritization strategies within the Prometheus environment are very flexible and can fit Customers' existing policy.

	considering the prioritization policy decided by the user. How is the prioritization of operations / work orders done? What type of prioritization policies are considered?	Order Types, Priority entries, Equipment Criticality, etc. can all be exploited and utilized to the business' advantage to ensure work is scheduling in accordance to Customers' standards. These priorities can be leveraged as part of the Auto-Level capabilities for automated scheduling.
	4.4. Automatic leveling of workload: level workload in order to balance resources, considering prioritizations. Does the software modify a work center scheduled in order to level workload? How is the workload leveling done? What type of prioritization policies are considered?	Simulation mode and Auto-Level capabilities allow quickly collaborating a resource-loaded schedule with respect to Work Center capacity and resource availability. Strategic methods can be incorporated, so Work Orders are scheduled by priority, preventive vs corrective, etc. Auto-leveling can be performed in respect to the same prioritization strategy mentioned above.
	4.5. Manual scheduling of capacity: allow the user to manually schedule capacity.	There are several means of manually adjusting schedule to meet resource capacity, including mass change, drag-and-drop, auto-level, etc.
	4.6. Summary of workload for each work center: provide summary information of each work center to the user. How is it calculated? Does it take into account only selected work orders or all work orders in SAP?	Selection variants can easily be established to provide full visibility into workload per Work Center. The Scheduler will dynamically display the amount of scheduled work over the available Work Center capacity, highlight any open areas in time as well as highlight any resource constraints for full visibility into resource utilization.
	4.7. Identification / scheduling of outsourced contractors: allow outsourced contractors (with or without SAP) to work with the Software Solution and to be treated as a work center. How can external contractors' capabilities be managed?	There are several strategies around incorporating external resources (contractors) into the scheduling process. Commonly, contractors are set up as separate Work Centers if resource capacity planning is required. Other options are to utilize different control keys at the operation level to define responsibility by an external party. These are both easily reflected in the <i>Prometheus Planning & Scheduling</i> solution
	4.8. Forcing work orders: allow the	Break-in work and emergency work can

	user to manually schedule work orders so as to force the system to provide the needed solution in case of emergencies.	easily be incorporated into the current maintenance schedule using the same functionalities described above: mass change, mass change dates & times, drag-and-drop scheduling, resource assignments, etc. Our solution will allow users to make these alterations to scheduling types in mass.
	4.9. Assignment Direction: allow the user to use the following assignation directions: forward, backwards for all work orders with lower urgency than the urgency threshold and according to the direction specified by the user in the initial definition.	All SAP Scheduling Types can be modified and reflected in the Prometheus Scheduling solution in respect to the different scheduling strategies as work progresses from the planning phase to the execution phase.
<u>5. Tracking</u>	5.1. Tracking of work: allow the user to track work orders in process.	Progress tracking capabilities exist in the <i>Prometheus Scheduling</i> solution for a quick visualization of work progression directly on the schedule.
	5.2. Ease of use to track work execution: provide information to easily get informed about the work order's progress.	Progress tracking capabilities exist in the <i>Prometheus Scheduling</i> solution for a quick visualization of work progression.
<u>6. Integration</u>	6.1. Integration with SAP: degree of integration between SAP and the Software Solution. Possibility of taking SAP PM's work orders as an input. How do the software integrate themselves?	Prometheus solutions integrate directly with SAP, utilizing SAP as the database and leverage core functionality within a simplified and highly configurable interface. With Prometheus Group's integration strategy, any changes from SAP will be immediately reflected in the Prometheus environment; and conversely, any changes to SAP data from the Prometheus environment are immediately communication back to SAP, which is maintained as the single point of truth database. Prometheus Group is an SAP certified development partner.

Supplementary Aspects: Implementation, Project and Training Overview

Project Approach & Work Plan


Prometheus Group applies the Critical Path Methodology for implementation projects to ensure timelines and milestones are met for new customer/product on-boarding. Please find *Prometheus Planning and Scheduling Implementation Project Plan* attached as supplemental documentation.

Project Team


Role	Company	Description
Project Manager	Prometheus Group	Prometheus Group's PM will organize meetings and ensure the project plan is following the appropriate timeline and sequence.
Implementation Manager	Prometheus Group	The implementation manager will perform the technical installation and configuration of all appropriate files/transforms for the project.
Principal Consultant	Prometheus Group	The principal consultant is an expert in SAP PM and is also an expert in maintenance processes and Prometheus solutions. This person will lead any workshops, trainings and ensure the solution is meeting requirements.
Account Executive	Prometheus Group	The account executive is the consistent contact for any additional information outside of the project and for continued management of the relationship with Customers.
Cloud Ops	Prometheus Group	The cloud ops team is responsible for setting up all hosted environments for the web solutions.
Project Manager/Lead	Customers	The project manager/lead for Customers is the main point of contact for Prometheus Group throughout this implementation and roll-out of the solution.
SAP Basis Resource	Customers	This resource is required for importing transforms and applying updates to the SAP landscape to ensure the integration is working properly.
SAP PM Security Resource	Customers	This resource is required for testing and sign-off of the solutions for moving transforms and updating and configuration identified during any implementation workshops.
SME	Customers	This individual ensures the decisions made are in the best interest of the requirements and processes for the Customers scheduling goals. They also are involved in UAT testing of solutions prior to go-live.
Personnel Management Admin	Customers	This resource is responsible for working with Prometheus Group to incorporate the identity

		management or login information to Prometheus solutions.
--	--	--

Prometheus Team Project Organization

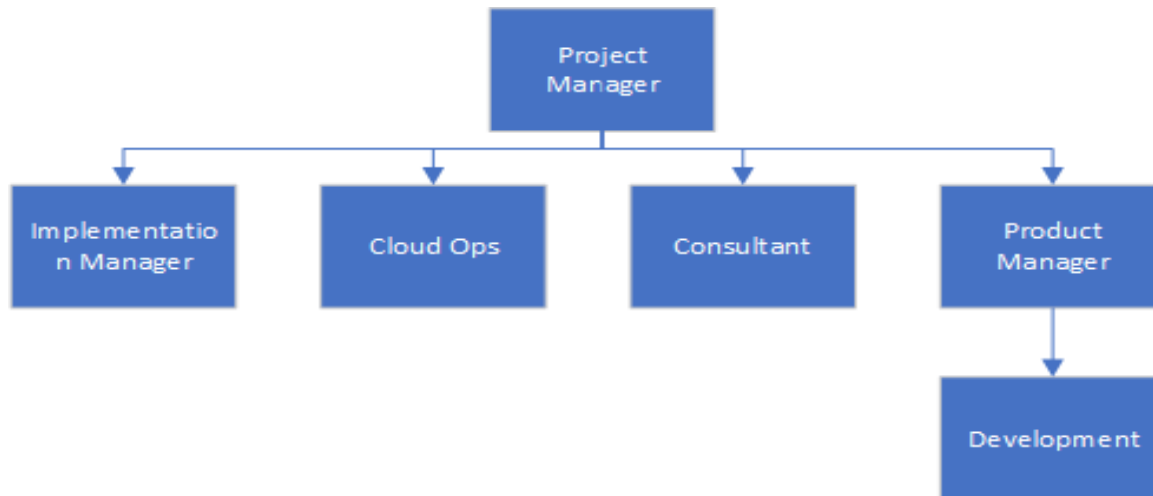

Customers Team Project Organization



Technical Implementation

Prometheus software is developed to ensure the implementation process is a seamless process and can be completed in a matter of weeks, not months. Prometheus will provide a dedicated Implementation Manager and Project Management team to support the customer project team in implementing the software into its IT environment. Our streamlined approach to the technical implementation offers our customers the following advantages:

- Reduces the impact to current IT landscape
- Reduces the amount of hardware required
- Faster, direct integration with source system

Change Management

Prometheus Group Consultants will lead a Process Discovery Workshop to understand current state of Customer's process and identify areas of impact. These areas of impact will be identified, and training guides/support documents can be built to help train on new process as well as product training during the end user training.

Communication Management

Prometheus Group will organize weekly meetings with the customer project implementation team to provide status updates and ensure transparency. As mentioned in other sections, Prometheus Project Managers and Account Managers can be contacted with ease via phone or email in the interim between weekly meetings.

Transition to Support

Once go live in the Production environment has taken place, there is a two-week Hypercare period during which the Project Implementation team and a dedicated Support representative perform frequent (daily or semi-weekly) check-ins with the customer to ensure that all identified issues are addressed promptly depending on criticality. Post-Hypercare, the dedicated Support representative will become the immediate point of contact.

Project Assumptions

- The customer will establish a dedicated Project Team
- Implementation is based on a single site roll-out
- Two environments will be provided
- One staging environment for QA/testing
- One Production environment
- All modules of the solution will be implemented in Production at the same time

Data Mitigation

The Prometheus Planning & Scheduling solution does not store customer data loaded from SAP. We utilize Remote Function Calls to query SAP data and to process any updates to SAP data in real time. With this streamlined connection with SAP, no SAP data is stored which negates any need to perform data migration from SAP to the solution.

Training

Following installation and configuration, Prometheus recommends on-site training for your users. End User training will be completed by a Prometheus Functional Consultant and are designed to employ industry best practice planning and scheduling processes driven by the effective use of our solutions.

Training is conducted onsite with user groups of no more than 12 at a time and is completed in 3-4 days. We recommend our customers adopt a “Super-User” training approach to assist with new user adoption and continued learning after the onsite training. Your training consultant will provide you with a training synopsis, which will include a review of what took place during the training, and any recommendations to assist with continued success. Prometheus Group also recommends regularly scheduled follow-up trainings to ensure maximize software adoption and continued advancement with our software.

The agenda below reflects key components in planning and scheduling best practices and Prometheus Planning & Scheduling Solution:

- **Work Order Planning** – Work Order selection, layout, list view, SAP Work Order planning review
- **Graphical Scheduler Overview** – User Status, Roles and Responsibilities (planner vs scheduler), drag and drop multiple work orders, Resource view on Planning View, Auto-level functionality, Work Centers (versions, intervals, adding Resources), Capacities, Mass Change
- **Continued Training in Production System** – Using Prometheus Scheduler to build out and advance schedules, sequencing jobs using Operation Relationships (hide, display, create, and modify),

Additional training can be purchased at any time. Additionally, other training opportunities include our Prometheus Group University (PGU) courses held throughout the year, our annual Prometheus Group User Conference, as well as our client portal, which is available at any time to the client for quick reference.

Software Maintenance and Support (Included with Annual Subscription)

Prometheus has support offices in the US, UK, and Australia that offer customer support availability 24 X 7. Most minor/major support issues can be handled during normal business hours – Monday to Friday (excluding public holidays), 0800 to 1700 EST/GMT/AEST, as appropriate for customer location. However, should a critical issue arise, defined as anomalies that prevent the successful routine use of the software and prevent users from using the functionality of the software, a global Prometheus customer success representative will provide an immediate response time (no longer than two hours) to address the issue.

Major software upgrades are available to our customers twice per year and are included in the annual maintenance fees. New releases include new functionality as well as the roll up of any minor releases for bug fixes, performance enhancements, etc. Patches/bug fixes and upgrades are applied via a standard SAP transport. Once the transport is received, the customer will be responsible for importing this transport into the SAP system. Prometheus Group will provide all details on implementing any configuration changes required for the Prometheus programs and will provide an overview of any new functionality.

Training Service Breakdown

1. Fit-Gap Analysis – 3 days on-site to understand the client’s current maintenance processes and how they will be carried out with the Prometheus Scheduling Solution. A report will be emitted the following week.
2. Training Week 1 – Initial training of end-users on the Scheduling solution
3. Training Week 2 – Follow up training in production with end-users

A detailed Project Plan for the Implementation Services was included with the proposal, but the general milestones and tasks required for the implementation are as follows:

- Send SAP Transports, Application Installation files, and License Keys. Import the SAP transports into each environment
- Install Planning and Scheduling Web Application on Servers.
(Development/Test/Production)
- Configure SAP <> Planning Scheduling solution connections for each environment
(Development/Test/Production)
- Configure Single Sign On (Active Directory/LDAP) authentication for Planning and Scheduling (Development/Test/Production)
- SAP and Web Application configuration
- Roles & Authorization building

Agustín Polverigiani—Account Manager, South America
apolverigiani@prometheusgroup.com
+54 9 11 5653 - 7052 (mobile)
